



# **The Billy Bishop Toronto City Airport Tunnel Project**

## **Tunnel Construction Committee Meeting #14**

**Tuesday May 27, 2014**

# Agenda

- |    |                        |       |
|----|------------------------|-------|
| 1. | Review of Minutes      | Forum |
| 2. | Two Month Look Back    | Forum |
| 3. | Two Month Look Ahead   | Forum |
| 4. | Questions & Discussion | All   |
| 5. | Next Meeting           | TPA   |

# 1. Review of Minutes

## MEETING MINUTES



**Topic:** Tunnel Construction Committee Meeting Number 13 – March 27, 2014

**Location:** [Harbourfront Community Centre](#)

**Attendees:**

|                               |   |
|-------------------------------|---|
| Ryan Gow                      | Forum Equity Partners Inc.              |
| Ken Lundy                     | Toronto Port Authority                  |
| Gene Cabral                   | Toronto Port Authority                  |
| Deborah Wilson                | Toronto Port Authority                  |
| Russ Martin                   | PCL Constructors                        |
| Mario Silva                   | TDSB                                    |
| <a href="#">Heino Molls</a>   | Bathurst Quay Neighbourhood Association |
| Hal Beck                      | Bathurst Quay Neighbourhood Association |
| <a href="#">Henry Piersig</a> | Bathurst Quay Neighbourhood Association |

**Distribution:**

|                                      |  |
|--------------------------------------|--|
| Attendees                            | TDSB   |
| Mario Silva                          | St. Stephen's Waterfront Daycare                 |
| Charlotte Sam                        | The Waterfront School Parent Council             |
| <a href="#">Kathryn Exner</a>        | City of Toronto, Waterfront Secretariat          |
| Christopher Dunn                     | City of Toronto, Municipal Licensing & Standards |
| Kimberley Kilburn                    | PCL Constructors                                 |
| Ken Shier                            | Ministry of the Environment                      |
| <a href="#">Rudy Pirosko</a>         | Toronto Public Health                            |
| <a href="#">Barb Lachapelle</a>      | The Waterfront School                            |
| Karen Barnes                         | Bathurst Quay Neighbourhood Association          |
| John Horne                           | <a href="#">Harbourfront Community Centre</a>    |
| Leona Rodall                         | City School                                      |
| <a href="#">Gabriela Kurzydowski</a> | Ministry of the Environment                      |
| Rod Adams                            | The Waterfront School                            |
| Paula <a href="#">Budhall</a>        | Bathurst Quay Neighborhood Association           |
| Joseph <a href="#">Svec</a>          | City School Parent Council                       |
| Beverly <a href="#">Dywan</a>        | Bathurst Quay Neighborhood Association           |
| Joan Prowse                          | The Waterfront School Parent Council             |
| Jackie Garrison                      |  |


**Date:** March 27, 2014 (19:00 – 21:00)

### ACTION ITEMS

| No. | Action  | Responsible | Status / TCD |
|-----|---|-------------|--------------|
| 1   | Presentations to be circulated to all attendees following TCC Meeting (See Attachment 1). | Forum       | Complete     |

## 2. Two Month Look-Back

1. Ice was removed from mainland shaft.
2. Ice was removed from island shaft.
3. CCTC roof and curtain wall framing were completed.
4. 90% of tunnel crown pours were completed.

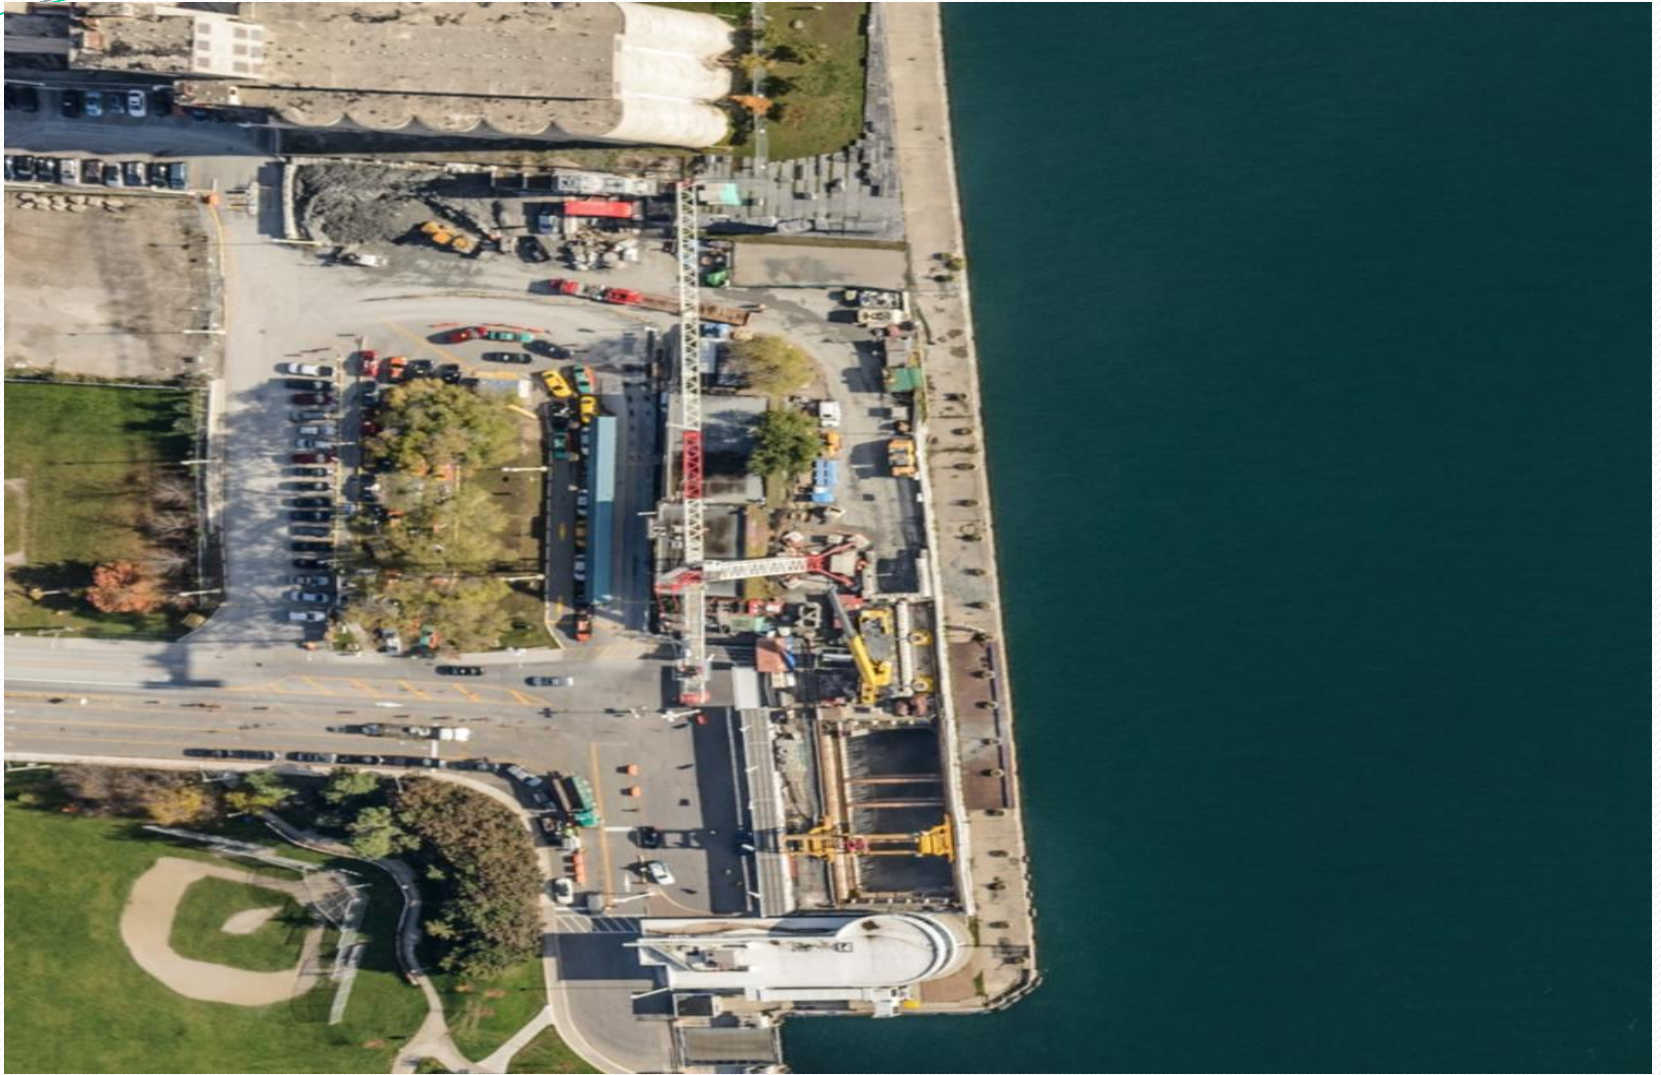

Mainland Site



Island Site



Ice Removal in Shaft



Tunnel



# 3. Two Month Look-Ahead

1. Tunnel formwork will be completed and removed from site.
2. Tunnel moving walks will start to arrive and be hosted down into tunnel.
3. Mainland shaft final excavation will be completed.
4. Mainland shaft waterproofing, rebar and formwork will be started.
5. Gantry crane will be removed.
6. Concrete batch plant will be removed from site.
7. Island shaft waterproofing, rebar and concrete formwork will be underway.
8. Island stair caisson wall shoring will be started.



# 5. Questions & Discussion



# 7. Next Meeting

To Be Determined at the Harbourfont Community Centre.
